



Monthly IntelSat ESO Update

Tom McNamara | SVP, Commercial Programs


26 May 2023



Program Updates

Wrapping up the program

- As of today, we are 95% filtered for Phase 2 and 100% scheduled for remaining sites
- We expect to complete filtering in late June and to certify in the first two weeks of July

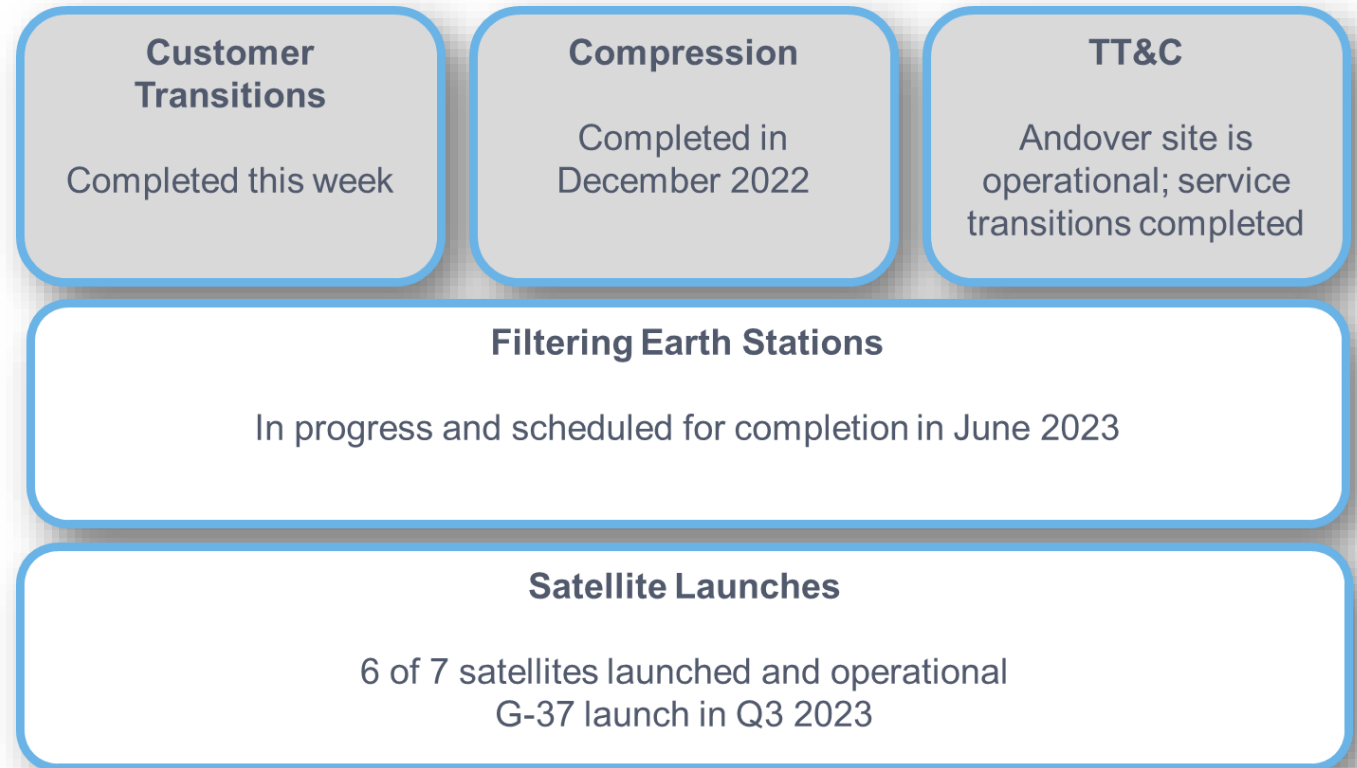

What comes next?

Certification and what follows


- Once the spectrum is clear and the earth stations are protected, each SSO certifies that they have completed the clearing
- Certification attestations are part of the public record for a period
 - “Validation” occurs once there are no credible challenges to the certification for 30 days
 - No challenges in Phase 1 and none expected in Phase 2
- So, when do the operators get the spectrum for 5G?
 - There is some debate around when the spectrum is available to overlay licensees (at certification, at validation, other), but we suggest you leave that to the lawyers
 - Please complete any outstanding work before July 1 to avoid disruption to your services


Upcoming Spectrum Shuffle

Freq Range	Interim Assignments	Final Assignments
4001-4200*	FSS	FSS
3981-4000	FSS	XXXXXXXXXXXXXXXXXX
3961-3980	FSS	T-Mo
3941-3960	FSS	T-Mo
3921-3940	FSS	ATT
3901-3920	FSS	ATT
3881-3900	FSS	ATT
3861-3880	FSS	ATT
3841-3860	FSS	VZ
3821-3840	FSS	VZ
3801-3820	XXXXXXXXXXXXXXXXXX	VZ
3781-3800	ATT	VZ
3761-3780	ATT	VZ
3741-3760	VZ	VZ
3721-3740	VZ	VZ
3700-3720	VZ	VZ

Assignments: Salt Lake City - PEA 27

Phase II Ground Clearing Roadmap

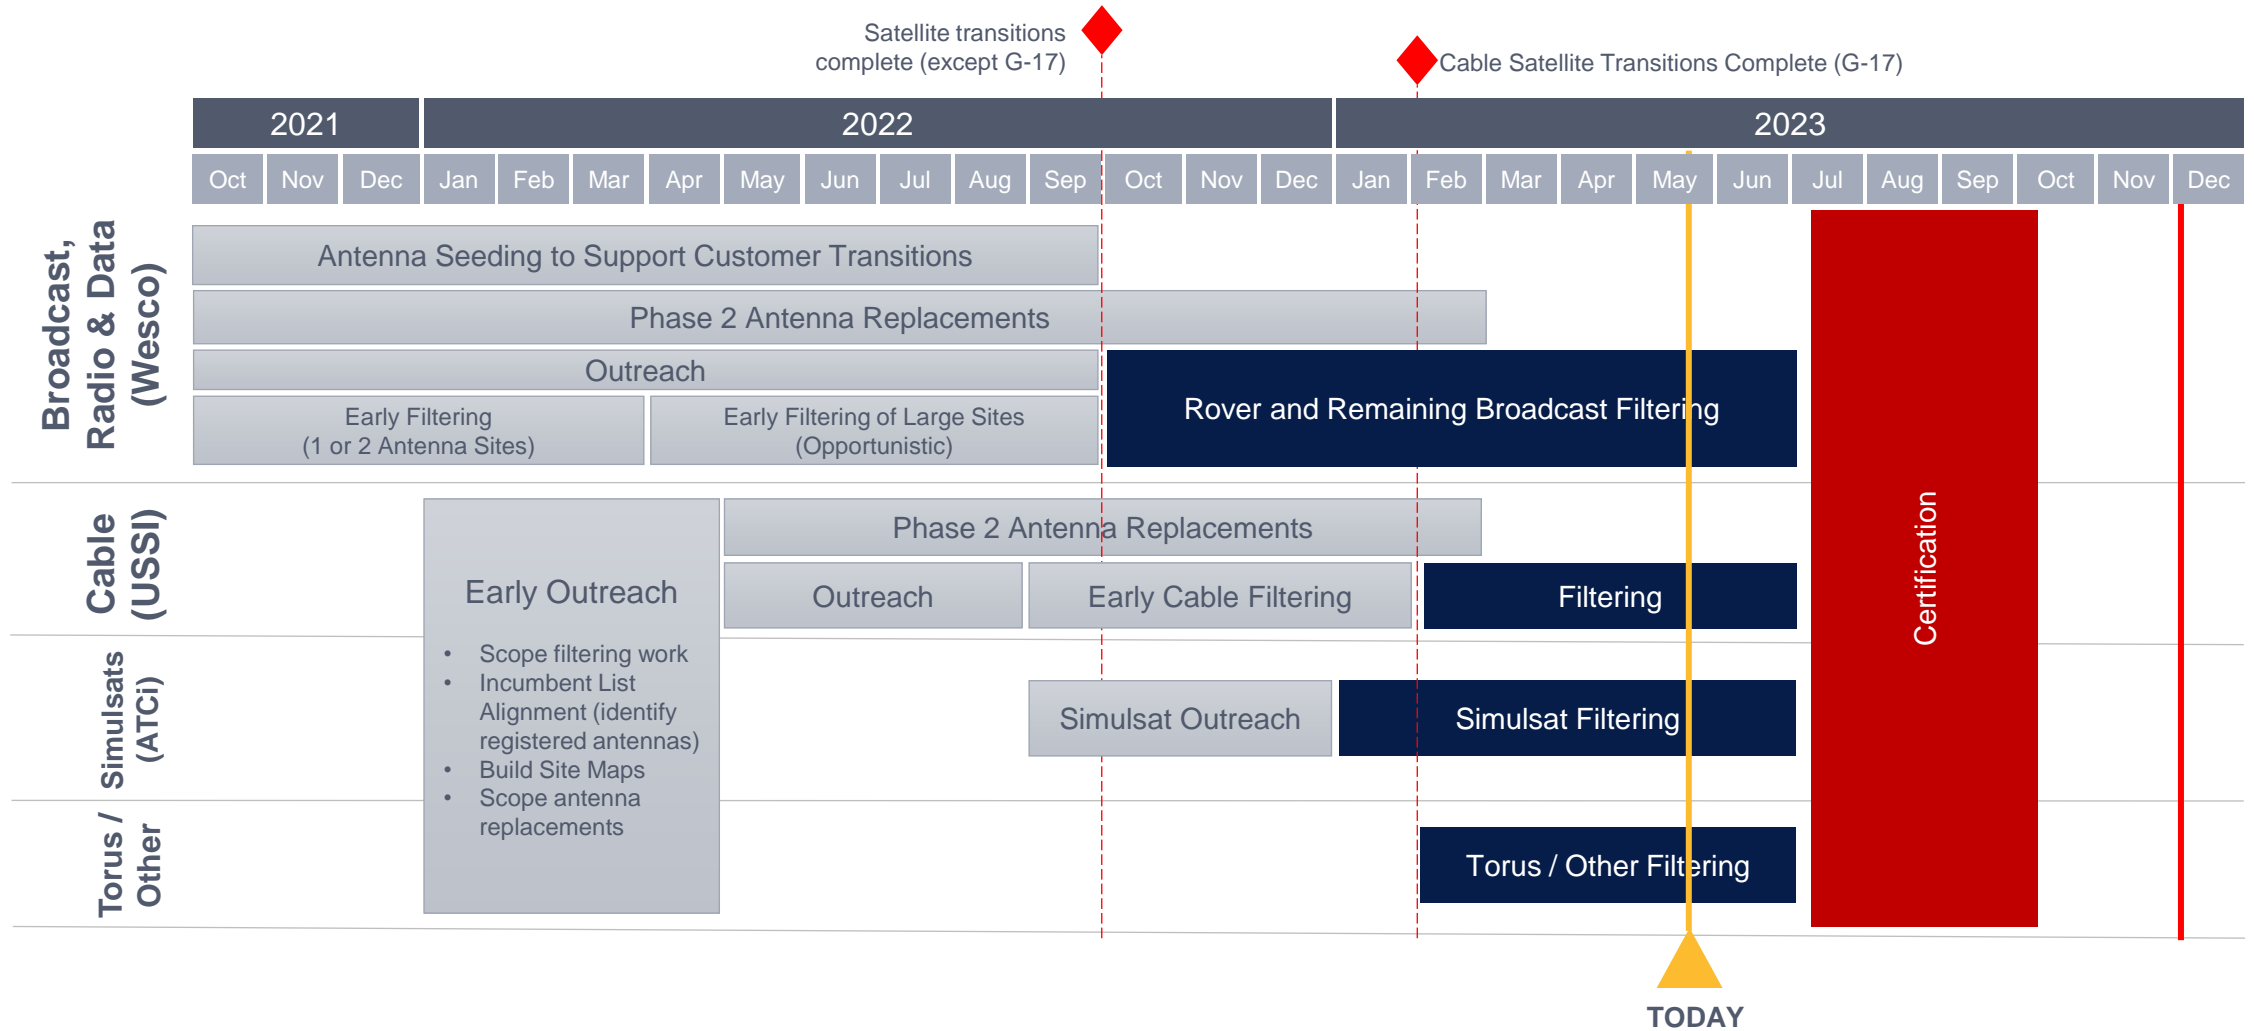



How To Contact Us

Tom McNamara – SVP, Commercial Programs

tom.mcnamara@intelsat.com

Transition Website: <http://intelsatcbandtransition.com>

Email: cbandinfo@intelsat.com
