

-43.4668°


170.1882°

Monthly Intelsat ESO Update

Tom McNamara | VP, C-Band Transition Management

March 4, 2021

Additional 2021 Critical Activities

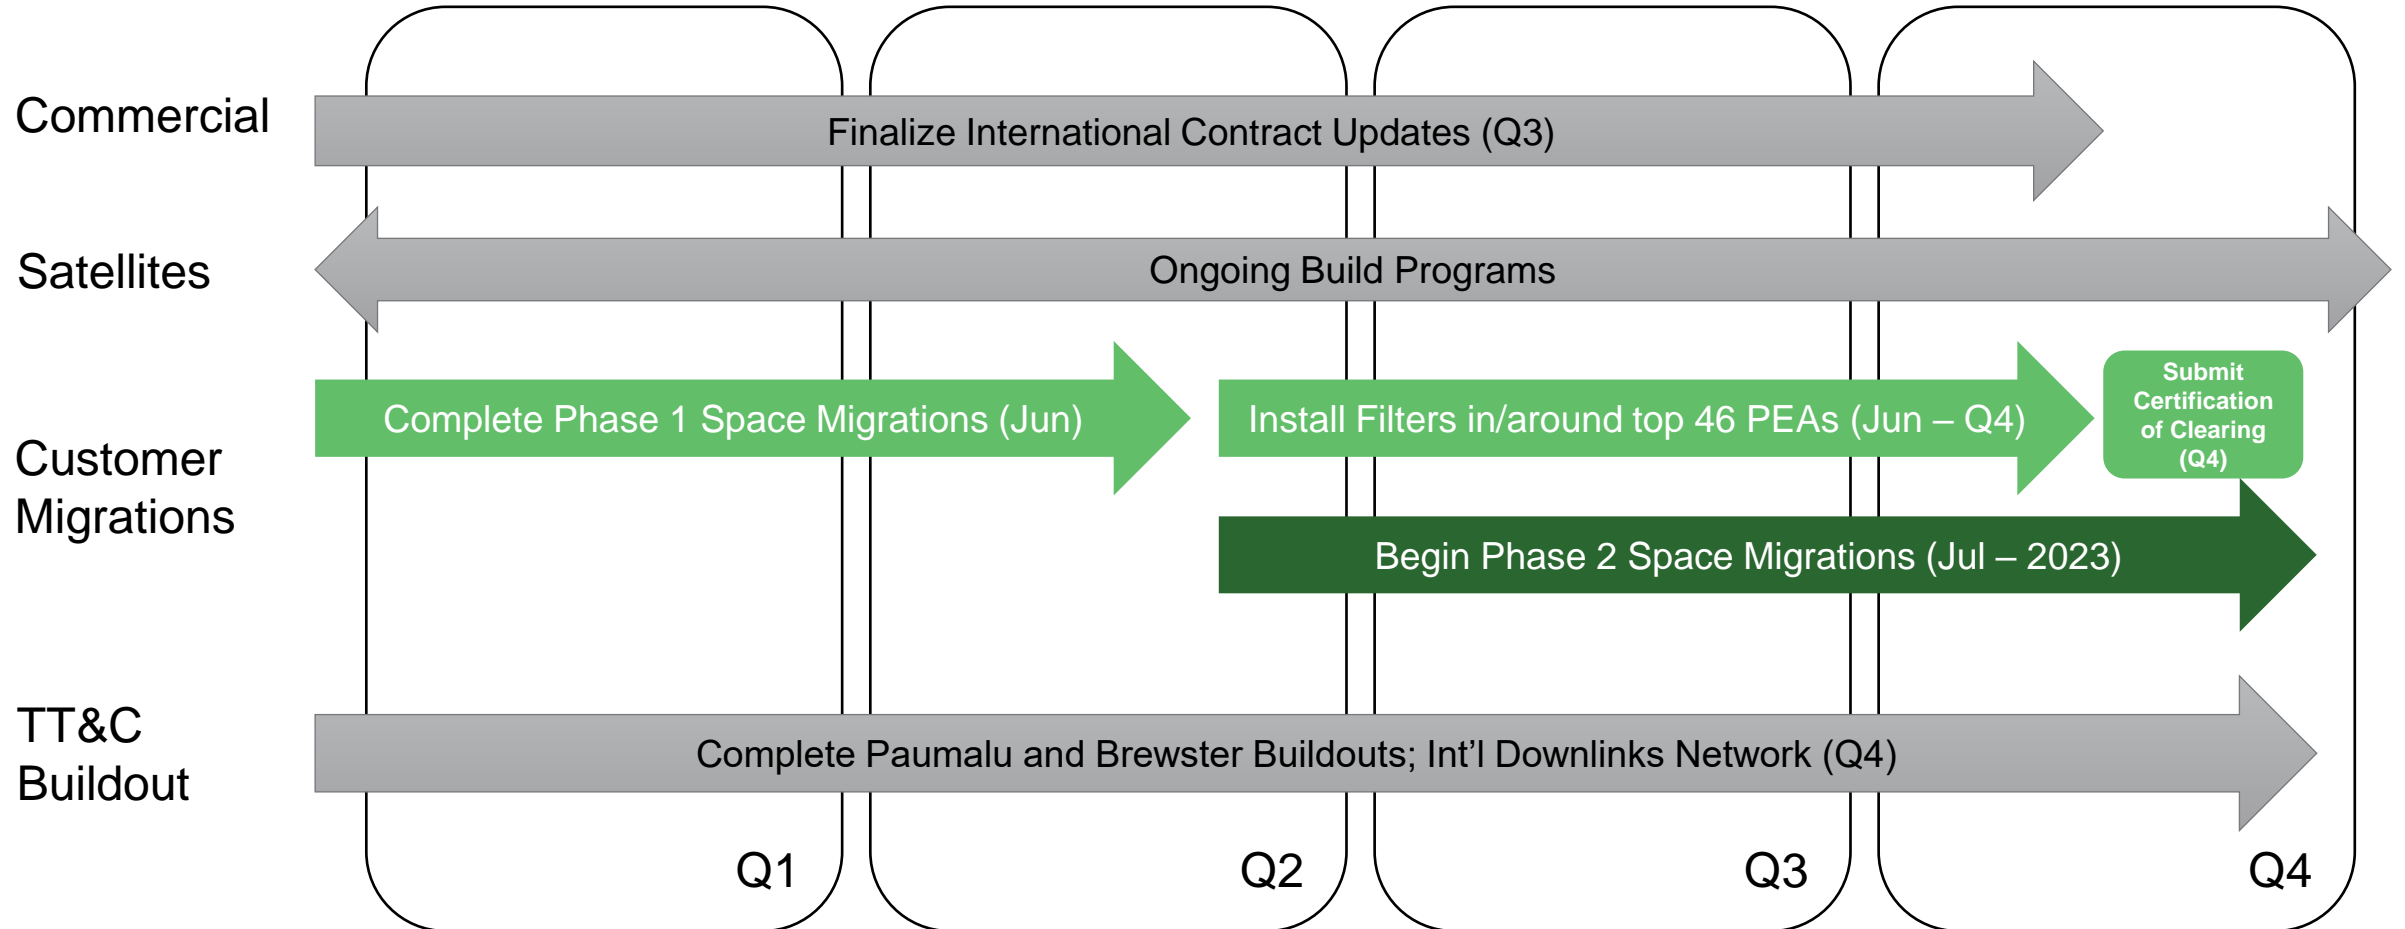

Transitions Progress

- Technology upgrade shipments are progressing well
 - Disney T0/T1 transition – ~80%80% shipped to date
 - Sinclair Transition 1 – ~70% units shipped to date
 - MLB transition – >90% of IRDs shipped to date
 - Activations of equipment steadily rising
- Intelsat MCPC platform and customers progressing
 - BBC/NHK deadlines extended 3 weeks
- Antenna seeding underway to address G-18 needs and undersized antennas
 - More than 140 antennas installed to date

Transition plan details for 1H2021



Phase I Start Date	Duration (Days)	Phase I End Date	Change Type	Customer	Customer Transition #	Phase I Start Sat/Trx	Phase I End Sat/Trx	Technology Upgrade	Status
1st Quarter									
1-Jan-21	30	31-Jan-21	F	Rignet		G-19 17C	G-19 09C		Complete
28-Feb-21	0	28-Feb-21	R	GCI Restoration		G-13 12C	G-13 07C		Complete
1-Feb-21	30	26-Mar-21	F	BBC / Intelsat MCPC platform		G-13 04C	G-13 20C		On target
1-Feb-21	30	3-Mar-21	F	Caracol / Intelsat MCPC platform		G-13 04C	G-13 20C		Complete
1-Feb-21	30	26-Mar-21	F	NHK / Intelsat MCPC platform		G-13 04C	G-13 20C		On target
1-Feb-21	30	3-Mar-21	F	Mega Media / Intelsat MCPC platform		G-13 04C	G-13 20C		Complete
4-Mar-21	0	4-Mar-21	R	GCI Restoration		G-13 20C	G-13 04C		On target
1-Jan-21	90	31-Mar-20	C, F	Disney	Disney Transitions 0,1	G-14 11C	G-14 07C	HEVC	On target
1-Jan-21	90	31-Mar-20	C, S, P, F	Disney		G-15 02C	G-17 17C	HEVC	On target
1-Jan-21	90	31-Mar-20	C, P, F	Disney		G-17 02C	G-17 17C	HEVC	On target
1-Jan-21	90	31-Mar-20	C, F	FoxCorp	FoxCorp Transition 1	G-17 05C	G-17 21C	HEVC	On target
1-Jan-21	90	31-Mar-20	C	FoxCorp		G-15 10C	G-15 10C	HEVC	On target
1-Jan-21	90	31-Mar-20	C	FoxCorp		G-17 16C	G-17 16C	HEVC	On target
2nd Quarter									
1-Feb-21	90	2-Apr-21	S, F	AT&T Sports		G-17 20C	G-17 11C		On target
2-Mar-21	60	1-May-21	P, F	ShopHQ		G-14 03C	G-14 22C		On target
1-Feb-21	90	2-May-21	S, P, F	Trinity Broadcasting Network		G-14 01C	G-18 17C		On target
1-Feb-21	90	2-May-21	S, F	Comcast/NBC-U		G-14 04C	G-18 19C		On target
1-Feb-21	90	2-May-21	C, S, F	MLB		G-13 01C	G-18 21C	HEVC	On target
1-Feb-21	90	2-May-21	C, S, F	MLB		G-17 04C	G-18 21C	HEVC	On target
1-Feb-21	90	2-May-21	S, F	IKO Media Group		G-23 24C	G-18 15C		On target
1-Mar-21	90	30-May-21	C, P, F	Sinclair	Sinclair Transition 1	G-15 04C	G-15 21C	HEVC	On target
1-Mar-21	90	30-May-21	C, F	Sinclair		G-15 20C	G-15 22C	HEVC	On target
1-Mar-21	90	30-May-21	F	Sinclair		G-15 11C	G-15 21C	HEVC	On target
1-Mar-21	90	30-May-21	F	Sinclair		G-15 12C	G-15 22C	HEVC	On target
1-Mar-21	90	30-May-21	S, P, F	CenturyLink		G-23 04C	G-13 19C		On target
1-Apr-21	30	31-May-21	P, F	ATCi		G-16 06C	G-16 15C		On target
1-May-21	30	31-May-21	F	US Government		G-13 17C	G-13 05C		On target
5-Dec-19	548	5-Jun-21	C, F	NPR		G-16 01C	G-16 23C	Audio	On target
5-Dec-19	548	5-Jun-21	C	NPR		G-16 23C	G-16 23C	Audio	On target
1-Apr-21	90	31-Jun-20	C, S, P, F	Disney	Disney Transition 2	G-14 14C	G-18 24C	HEVC	On target
2-Apr-21	90	31-Jun-20	S, P, F	Overon		G-23 24C	G-23 22C		Complete

- BBC/NHK migrations extended until 26-Mar-2021

- Items in blue are in dual illumination and the transitions continue

- Items in orange just began or are about to begin dual illumination

Key takeaways

- We have recently refreshed the microsite, please visit <https://intelsatcbandtransition.com/>
- Most of the **filtering will not start until June 1, 2021** and it will only happen in and around the top 46 markets then. Nationwide filtering will start in earnest mid-year 2023.
- The focus for the first half of 2021 is **grooming services** on the satellite – frequency, pol and satellite changes – **and installing compression equipment.**
- If you have questions, **please email us** at cbandinfo@intelsat.com and we will be happy to answer them.
